


GRAFIC GANTT

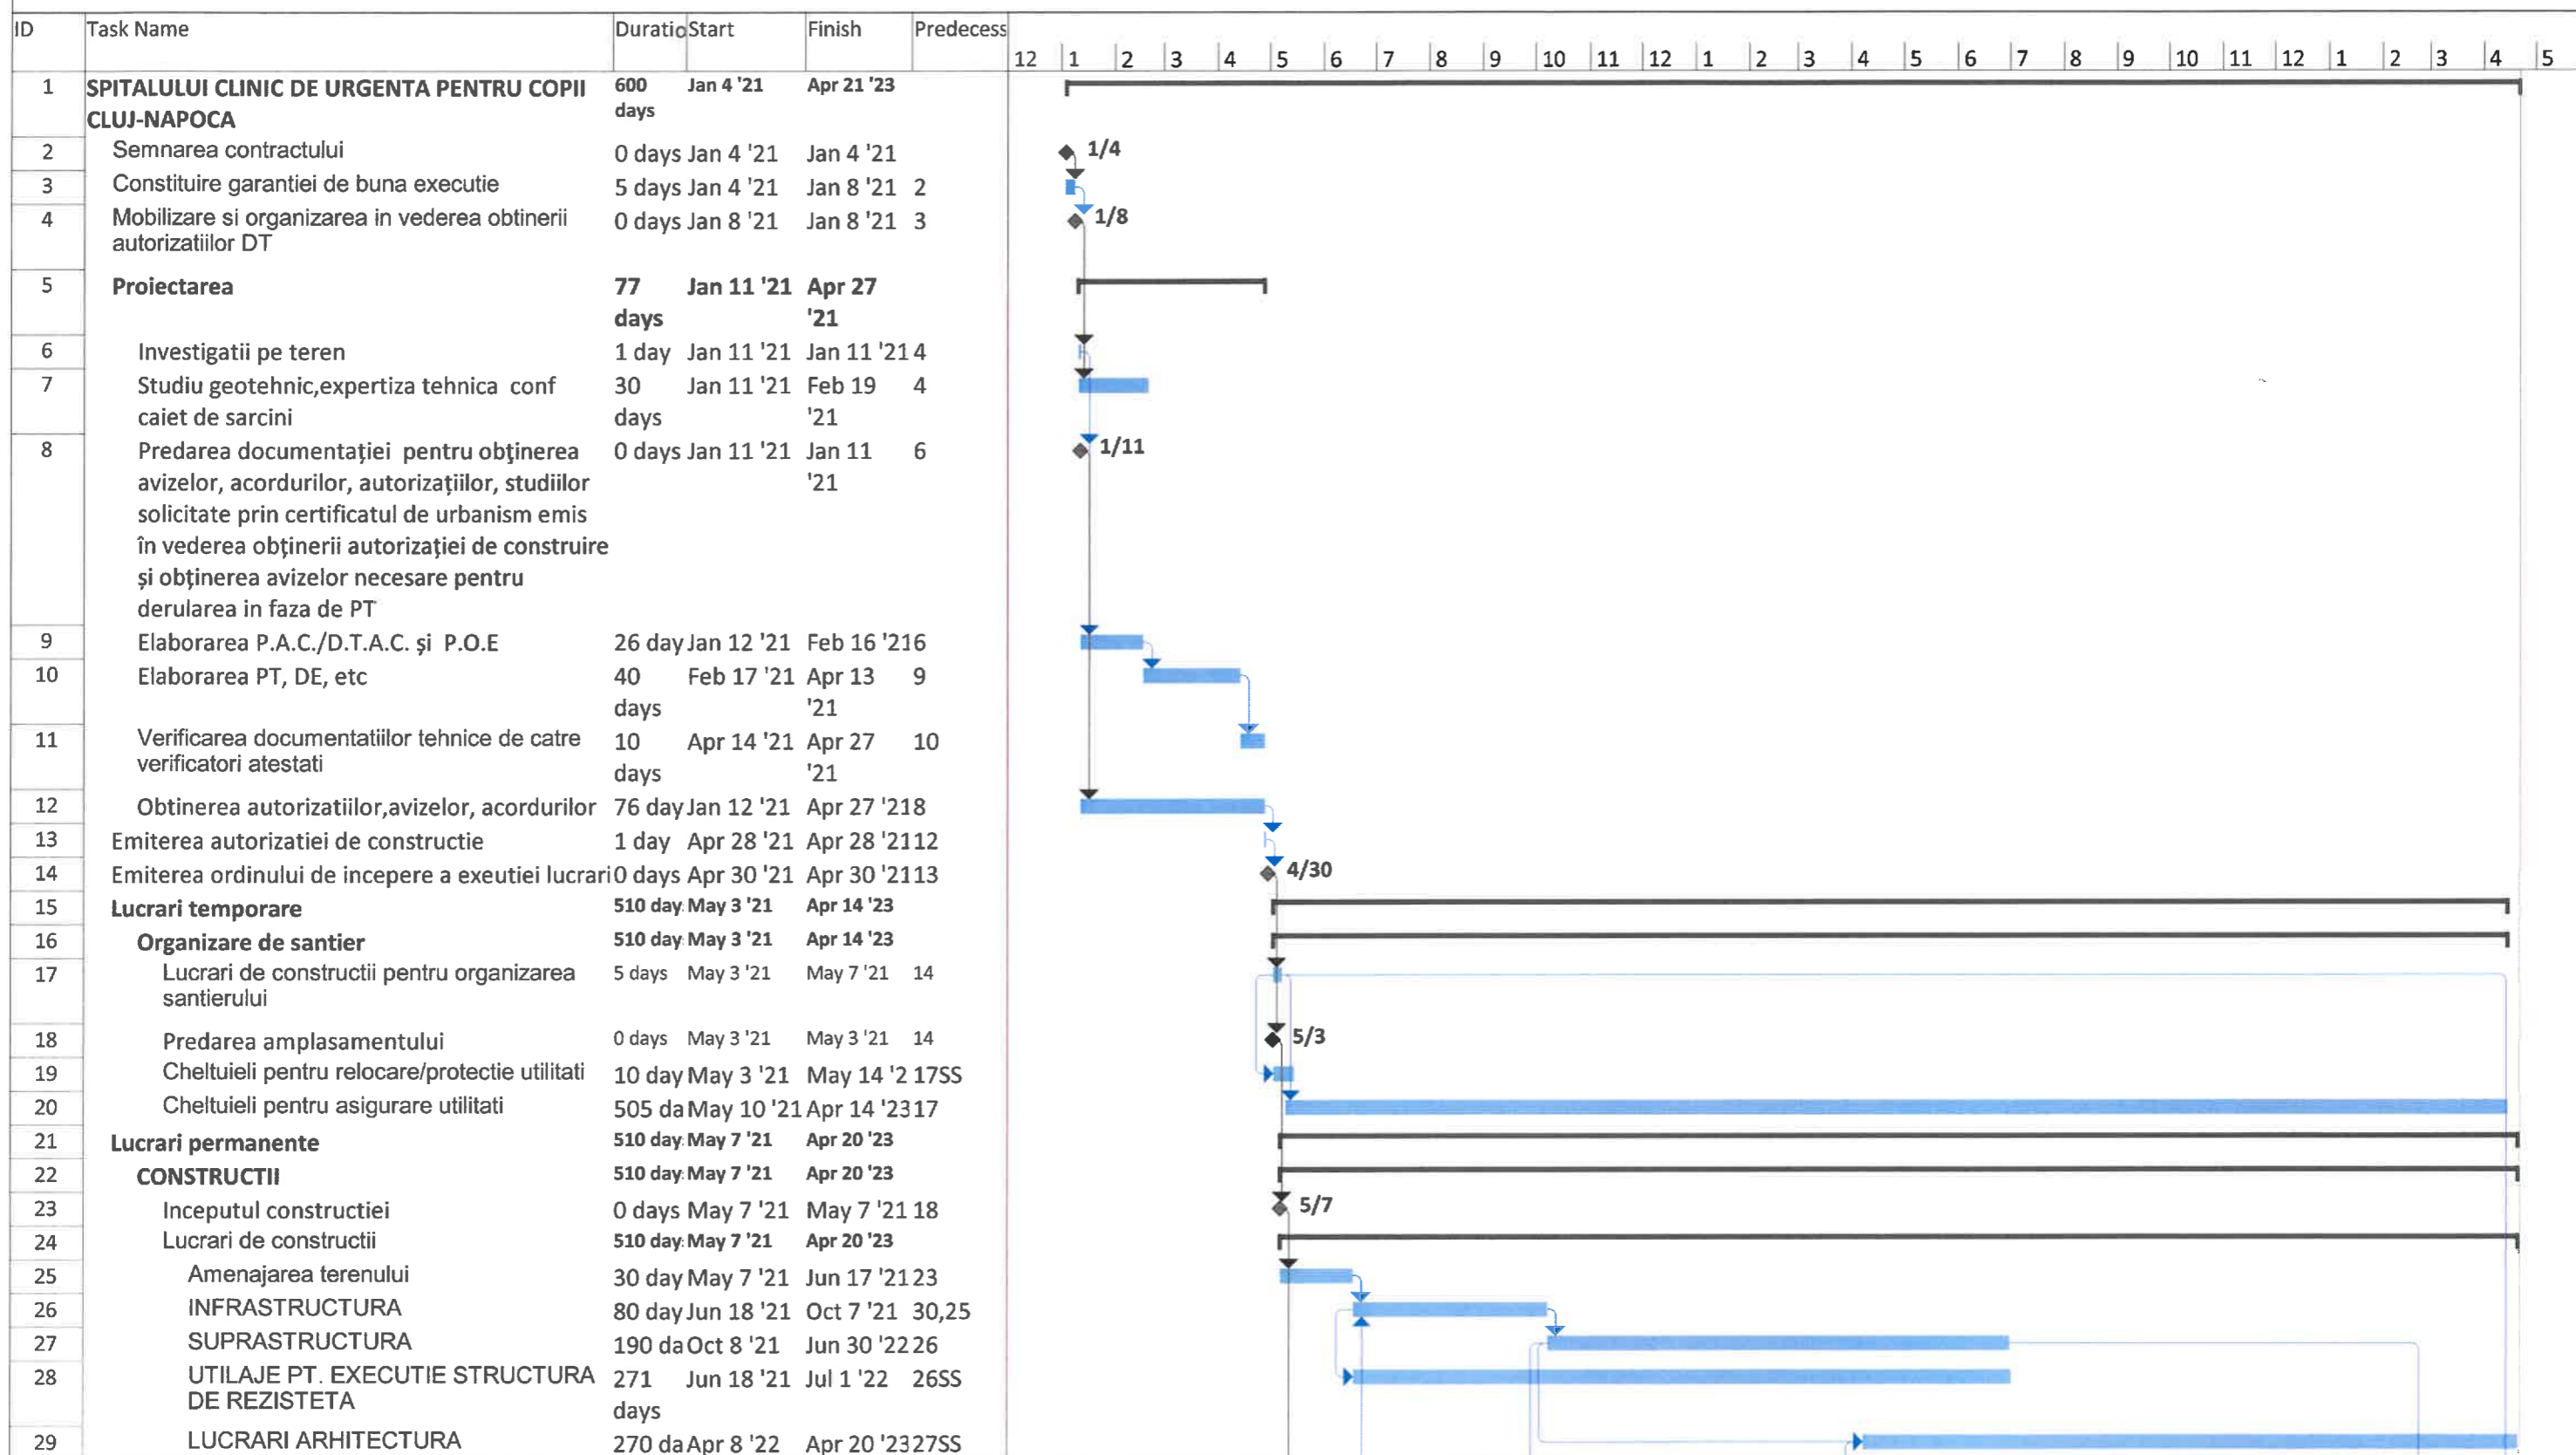

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only		Manual Progress	
Summary		Inactive Task		Duration-only		Finish-only			

GRAFIC GANTT


ID	Task Name	Duratio	Start	Finish	Predecess	12	1	2	3	4	5	6	7	8	9	10	11	12	1	2	3	4	5	6	7	8	9	10	11	12	1	2	3	4	5
30	LUCRARI DEMOLARI, DESFACERI INTERIOR-EXTERIOR	30 days	May 7 '21	Jun 17 '21	23																														
31	Asigurarea procesului control calitate, intocmirea documentelor de calitate conform legislatiei	510 days	May 7 '21	Apr 20 '23	30SS																														
32	LUCRARI DE INSTALATII	350 day	Oct 8 '21	Feb 9 '23																															
33	INSTALATII SANITARE INTERIOARE SI EXTERIOARE	320 days	Oct 8 '21	Dec 29 '22	27SS																														
34	INSTALATII TERMICE	330 da	Oct 8 '21	Jan 12 '23	27SS																														
35	INSTALATII ELECTRICE	330 da	Oct 8 '21	Jan 12 '23	27SS																														
36	INSTALATII CURENTI SLABI VOCE-DA	220 da	Apr 8 '22	Feb 9 '23	29SS																														
37	INSTALATII AVERTIZARE INCENDIU	220 da	Apr 8 '22	Feb 9 '23	29SS																														
38	INSTALATII SUPRAVEGHERE VIDEO	220 da	Apr 8 '22	Feb 9 '23	29SS																														
39	INSTALATII CONTROL ACCES	220 da	Apr 8 '22	Feb 9 '23	29SS																														
40	INSTALATII SONORIZARE	220 da	Apr 8 '22	Feb 9 '23	29SS																														
41	INSTALATII CLIMATIZARE	220 da	Apr 8 '22	Feb 9 '23	29SS																														
42	INSTALATII ALIMENTARE CU GAZ	120 da	Oct 8 '21	Mar 24 '22	27SS																														
43	Asigurarea procesului control calitate, intocmirea documentelor de calitate conform legislatiei	350 days	Oct 8 '21	Feb 9 '23	33SS																														
44	Montaj utilaje, echipamente tehnologice si functionale	61 days	Dec 30 '22	Mar 24 '23																															
45	MONTAJ UTILAJE SI ECHIPAMENTE TEHNOLOGICE INSTALATII SANITARE	30 days	Dec 30 '22	Feb 9 '23	33																														
46	MONTAJ UTILAJE SI ECHIPAMENTE TEHNOLOGICE INSTALATII TERMICE	30 days	Jan 13 '23	Feb 23 '23	34																														
47	MONTAJ UTILAJE SI ECHIPAMENTE TEHNOLOGICE INSTALATII ELECTRICE	30 days	Jan 13 '23	Feb 23 '23	35																														
48	MONTAJ UTILAJE SI ECHIPAMENTE TEHNOLOGICE INSTALATII CLIMATIZARE	30 days	Feb 10 '23	Mar 23 '23	41																														
49	MONTAJ UTILAJE SI ECHIPAMENTE TEHNOLOGICE INSTALATII GAZ	30 days	Feb 13 '23	Mar 24 '23	42																														
50	Utilaje, echipamente tehnologice si functionale care necesita montaj	61 days	Dec 30 '22	Mar 24 '23																															
51	MONTAJ UTILAJE SI ECHIPAMENTE TEHNOLOGICE INSTALATII SANITARE	30 days	Dec 30 '22	Feb 9 '23	45SS																														
52	MONTAJ UTILAJE SI ECHIPAMENTE TEHNOLOGICE INSTALATII TERMICE	30 days	Jan 13 '23	Feb 23 '23	46SS																														
53	MONTAJ UTILAJE SI ECHIPAMENTE TEHNOLOGICE INSTALATII ELECTRICE	30 days	Jan 13 '23	Feb 23 '23	47SS																														
54	MONTAJ UTILAJE SI ECHIPAMENTE TEHNOLOGICE INSTALATII CLIMATIZARE	30 days	Feb 10 '23	Mar 23 '23	48SS																														
55	MONTAJ UTILAJE SI ECHIPAMENTE TEHNOLOGICE INSTALATII GAZ	30 days	Feb 13 '23	Mar 24 '23	49SS																														



Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only		Manual Progress	
Summary		Inactive Task		Duration-only		Finish-only			

GRAFIC GANTT

ID	Task Name	Duratio	Start	Finish	Predecess
56	Amenajare pentru protectia mediului	40 day	Feb 22 '23	Apr 18 '23	27
57	Verificari, probe, teste conform programului de control calitate	510 days	May 7 '21	Apr 20 '23	23
58	Activitati de prevenire atenuare eliminare riscur	510 da	May 7 '21	Apr 20 '23	23
59	Masuri de protectie pt desfasurarea activitatii cu respectarea reglementarilor in vigoare	510 days	May 7 '21	Apr 20 '23	23
60	Verificare si masuri privind riscurile prevazute in metodologie	510 days	May 7 '21	Apr 20 '23	23
61	Rapoarte, documente pt cartea constructiei,detalii de executie	510 days	May 7 '21	Apr 20 '23	23
62	Asistenta tehnica din partea proiectantului/Interventie specialisti	510 days	May 7 '21	Apr 20 '23	23
63	Verificarea documentelor de catre Inginer	83 days	May 7 '21	Apr 20 '23	23
64	Dezafectarea organizarii de santier	5 days	Apr 14 '23	Apr 20 '23	17
65	Receptie lucrare	0 days	Apr 21 '23	Apr 21 '23	63,57,61
66	Predarea documentației revizuite as built	0 days	Apr 21 '23	Apr 21 '23	65
67	Nota: Perioada de proiectare este de 4 luni; iar cea de executie este de 24 luni!				
68	Nota: Perioada de garantie este de 120 de luni !				

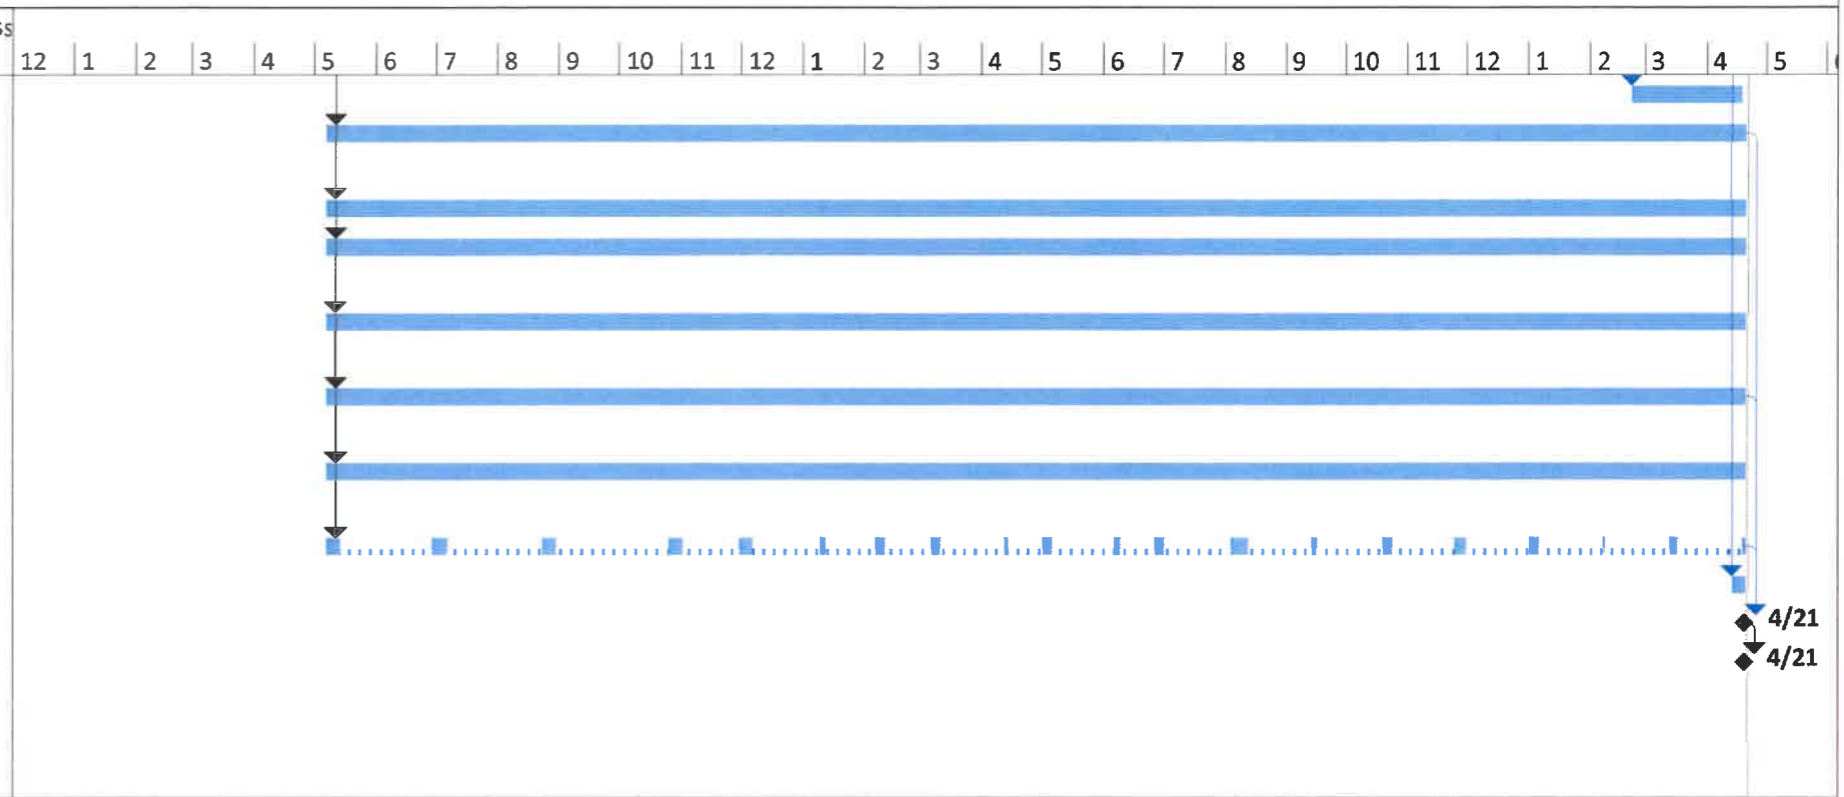

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only		Manual Progress	
Summary		Inactive Task		Duration-only		Finish-only			
